

**2nd Work report**  
**on the construction of two buildings with a total of 6 classrooms,**  
**office, storage room and toilets**  
**for the primary school of AGONMEY**

**Friday, December 29, 2023**

The plastering work on the second building had already started the day before. 2 gable sides were plastered. Today more 2 gable sides in the 2nd class room are being plastered.



**Saturday, December 30, 2023**

The plastering work in the office began on the first building.

On the 2nd building 2 side-walls are plastered.

The anti-burglary devices are delivered.

**Wednesday, January 3, 2024**

After the New Year celebrations, the bricklayers renewed the scaffolding and prepared everything for work to begin.

**Thursday, January 4, 2024**

1st building : The office is plastered. In the storage room, 3 walls are plastered.

2nd building : work has begun under the veranda. 3 sections are plastered.

**Saturday, January 6, 2024**

1st building: 2 gable-walls of the 1st classroom are plastered,

The rear wall of the second building is plastered with sikalit and sikalatex.



### **Monday, January 8, 2024**

The second classroom in the first building is being plastered.

One side wall of the second building is plastered with sikalit and sikalatex.



### **Tuesday, January 9, 2024**

1st building: The 2nd classroom has been plastered and the gable sides of the 3rd classroom are being plastered.

2nd building: The 2<sup>nd</sup> outer gable end is plastered with Sikalit and Sikalatex.

The veranda is also being worked on.

In the evening, the association's treasurer comes to the construction site to inspect the progress of the work.

The women returned to finish the remaining filling work.

### **Wednesday, January 10, 2024**

1st building: The 3rd classroom is plastered.

2nd Building: The outside has been plastered. Now the windows and door frames are neatly carved out. 3 pillars are also plastered.



### **Friday, January 12, 2024**

1st Building: The entire back and half of the side wall are plastered,

2nd building: 3 partial walls under the veranda and 4 pillars are plastered. Blackboards are put up.

The locksmiths attach the railings to the rampe.



### **Saturday, January 13, 2024**

1st Building: An outer side wall is plastered. 3 partial walls under the veranda and 3 pillars are plastered.


2nd building: 4 pillars and 4 wall overhangs at the back of the building to support the roof are plastered.



## **Monday, January 15, 2024**

1st Building: 3 more partial walls on the veranda and the 2 outside gable sides are plastered.

2nd Building; The pillars under the veranda are plastered.

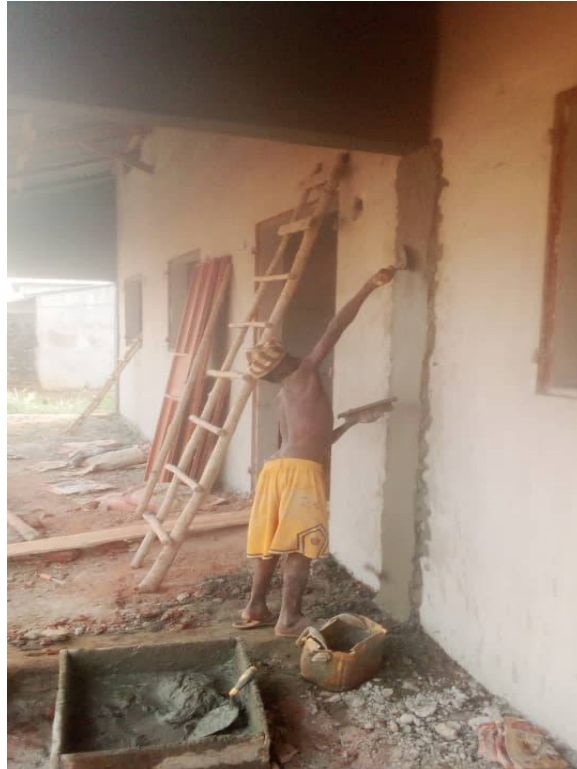

## **Tuesday, January 16, 2024**

The toilets are being plastered.

On the 1st building, partial walls on the veranda are plastered.

On the second building all the pillars are plastered.





### **Wednesday, January 17, 2024**

The toilet cubicles are plastered

The floors in the classrooms are compacted and prepared for cementing.



### **Thursday, January 18, 2024**

1st Building: All soils are compacted, leveled and marked.

2nd building: 2 rooms are cemented.

### **Friday, January 19, 2024**

1st Building: Office and storage room are cemented

2nd building: The 3rd room and the veranda are cemented.

Gravel is delivered in the evening.



## **Saturday, January 20, 2024**

The pillars of the ramps on both buildings have been cast.

The front of the toilet is plastered.

1st Building: The floors of 2 classrooms are cemented.

2nd Building: The staircases are plastered and cemented.

## **Tuesday, January 23, 2024**

1st building: the floor of the 3rd classroom and the veranda are cemented

The walls of the flower beds are plastered.

In the evening the treasurer and the manager come to the construction site.



## **Mercredi 24 Januar 2024**

The ramp and staircases of the 1st building are cemented.



The toilet seats are placed.



### **Thursday, January 25, 2024**

The ramp of the 2nd building is cemented.

The gables of the two roofs are sealed watertight with Sikalit and Sikalatex.



### **Friday, January 26, 2024**

The exhaust pipes are installed in the toilets. The steps are cemented

The burglary protection devices of the buildings are installed.



**Saturday, January 27, 2024**

The 3 protective grilles are installed in the office and in the storage room.



**Monday, January 29, 2024**

Small corrections continue to be made

The construction supervisor begins to clean up the construction site.

**Wednesday, January 31, 2024**

All masonry work has been completed.



The buildings are now waiting for their color change.

**Rapporteur :**

**Loko Joseph**
