


3rd work report
(September 6th, 2021 to October 6th, 2021)

**on the construction of one building holding 3 classrooms, office, storage and toilets
for the public primary school of Gbodjoko
District of Zinvié
municipality of Abomey-Calavi
Republic of Benin**

The toilet pit is finished by September 10th. The women of Gbodjoko come to the construction site to pour the sand that was extracted from the pit into the classrooms.



The masons begin to brick the toilet pit.

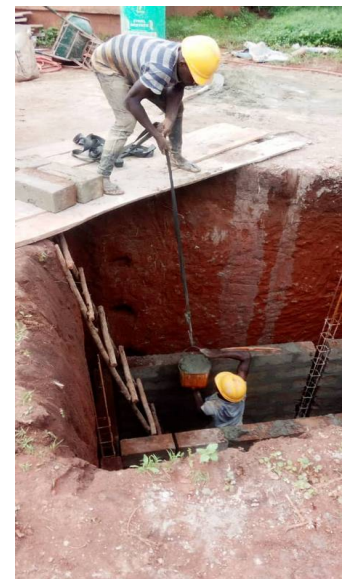



The toilet units are erected on the closure plate.



The toilet house is waiting for its roof.

After the classrooms have been filled with sand, the carpenters start making the roof truss. The roof is ready in no time.



The toilet seats have arrived. The doors and shutters are put in place.



The building is ready to be plastered.

Greetings from our construction site.
Astrid Toda
